

PRFUP20250671

Any public curb, gutter, or sidewalk broken now or during the course of construction shall be removed and replaced per City Standards.

Where a curb exists, the lateral offset of all vertical obstructions shall be a minimum of 1.5' from the face of the curb to the face of the vertical obstruction and a minimum of 3' at intersections. Where no curb exists, the lateral offset of all vertical obstructions shall be a minimum of 4' measured from the edge of pavement to the face of the obstruction.

Anchored guy wire shall be installed or retrofit with a minimum 7-feet of overhead sidewalk clearance. The guy-wire shall not obstruct access to any property or to a public or private utility facility. The guy wire shall be anchored in the public right-of-way or within a private utility easement.

City of Puyallup
Development & Permitting Services
ISSUED PERMIT

Building

Planning

Engineering

Public Works

Fire

Traffic

FOREMAN (CHECK BOX WHEN COMPLETED)

☐ PSE Equipment LOCKED/SECURED & Work Area left in CLEAN/SAFE Condition.

☐ Grid, Cable, and Switch numbers INSTALLED & VERIFIED.

☐ Field Changes RE-DRAWN on As-built.

☐ Material VERIFIED and CHANGES noted on Paperwork.

☐ Total PRIMARY Cable noted on As-built.

☐ Company ID#s RECORDED in correct location on As-built.

☐ Indicate correct FUSE SIZE on As-built & VERIFY proper PHASE.

☐ Correct QA Checklists reviewed.

☐ Deviations noted on the As-built and their reason.

☐ I certify that the work performed meets PSE's standards and procedures and that all quality requirements are met.

Foreman's Signature _____

Print Name _____ Date _____

PROJECT PHASE	NOTIF#	ORDER#
PWR Superior		
New Install		
SL Light	513381620	105101747
Removal		
Smart Node		141007880
Temporary		
Job Order		
GAS Distribution		
HP Main		
HP Svc/MS		
CABLE TV		
PHONE		

Project Manager Contact Information:

Mike Hammons


(425) 765-1395 Cell Phone

"Locates Required" Yes ☒ No ☐
"Outages Required" Yes ☐ No ☒
"Flagging Required" Yes ☒ No ☐

PSE STREET LIGHT NOTES

1. IN ALL SHOEBOX AND COBRAHEAD INSTALLATIONS, THE LUMINAIRE MUST BE LEVELED.

Vicinity Map
47.2152, -122.3111

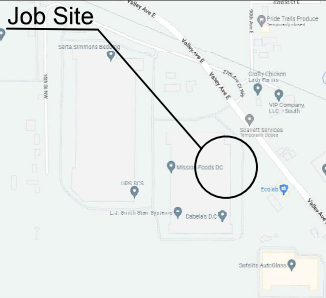

Owner / Developer Contact Info

Chuck E. Pierson 417-429-3729
1212 Valley Ave NW, CEPierson@basspro.com
Puyallup, WA 98371

For contacts below dial 1-888-CALL PSE (225-5773)

CALL (800) 424-5555
2 BUSINESS DAYS BEFORE YOU DIG

THIS SKETCH NOT TO BE RELIED UPON FOR EXACT LOCATION OF EXISTING FACILITIES

<input checked="" type="checkbox"/> NEW BUSINESS	<input type="checkbox"/> CORRECTIVE / 10 DAY WAIVED	REAL ESTATE/EASEMENT	PERMIT
		N/A	N/A
3		FUNCTION	CONTACT
2		ACCOUNT MGR	PHONE NO
1		ENGR - POWER	DATE
REV#	BY	DESCRIPTION	
COUNTY	Emer Sect	Gas Wk Ctr	POWER WK CTR
PIERCE			3515
1/4 SEC	OP MAP	PLAT MAP	
U-MAP NO (POWER)	OH CKT MAP	UG CKT MAP	CIRCUIT NO
2004E063	2004E056		CED-13
JOINT FACILITIES ARRANGEMENTS			
UTILITIES	N/A	N/A	N/A
CONTACT	N/A	N/A	N/A
PHONE#	N/A	N/A	N/A
Bass Pro shops			INCIDENT
INSTALL 3 NEW 30' WD POLE & (8) 121W LIGHT			MAOP
1212 Valley Ave NW, Puyallup, WA 98371			Gas Order
			Elect Order
			105101747
SCALE			PAGE
1"=60'			1 of 1

DESIGNED BY: PSE

CONSTRUCTION NOTES

- SL1 - SL4:
- INSTALL NEW 30' WOOD POLE CLASS 3
 - INSTALL 2 NEW 121W LED GALLEON & 4' ARM
 - MH@25'
 - ORIENT AS SHOWN
 - INSTALL SMART NODE AND SERIAL NUMBER
 - INSTALL STREET LIGHT TAG & GRID
 - FLAGGING REQUIRED

SPAN NOTES

- INSTALL 4 NEW SPAN OF #4 DPX BY DESIGN AND TABLE

SITE SPECIFIC NOTES

- SL1:
- POLE WILL BE INSTALLED IN PLANT STRIP/DIRT
- SL2, SL3 & SL4:
- POLE WILL BE INSTALLED ON THE ASPHALT AND SAW CUTTING WILL BE REQUIRED

MAPS AND RECORDS NOTES:


UPDATE ESRI TO REFLECT THE NEW GRIDS AND POLES.

STREET LIGHT TABLE

SITE #	GRID #	TAG #	TYPE	MTG HT.	ARM	LUMINAIRE		WO #	BILLING SCH.	SMART STREET LIGHT NODE	TOTAL CONN LOAD	NOTES
						WATTS	STYLE					
SL1A	569158 155055		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL1B	569158 155055		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL2A	569145 155053		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL2B	569145 155053		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL3A	569134 155055		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL3B	569134 155055		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL4A	569121 155055		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	
SL4B	569121 155055		NEW WD POLE	25'	4'	121 W	LED GALLEON FORWARD THROWT	105101747	58		120/240	

OH CIRCUITRY TABLE

LOCATION		Size (Wire)	Design Length (ft)	Actual Length (ft)
From	To			
P01	SL1	#4 DPX	70	
SL1	SL2	#4 DPX	125	
SL2	SL3	#4 DPX	125	
SL3	SL4	#4 DPX	110	
TOTAL			430	

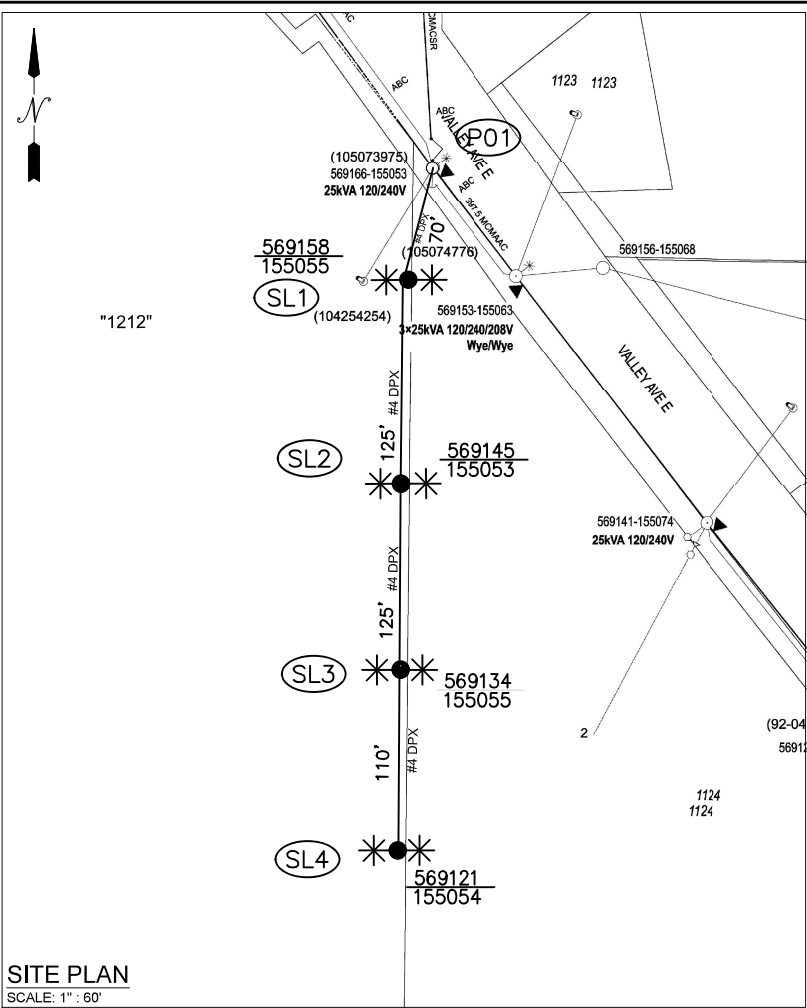

SITE PLAN
SCALE: 1" = 60'
