

POLE TRANSFER OF CENTURYLINK FACILITIES FROM OLD POLES TO NEW FOREIGN POLES

State: WASHINGTON

Wire Center: PYLPWA01

Job #: P.118097.E.01

Address(es): 1603 3rd St SE

Asset Tag: A4341341




Section: 34 **Town:** 20N **Range:** 4E

Lat/Lon: 47.176459, -122.29101

X=OLD POLE

T=NEW FOREIGN POLE

N→

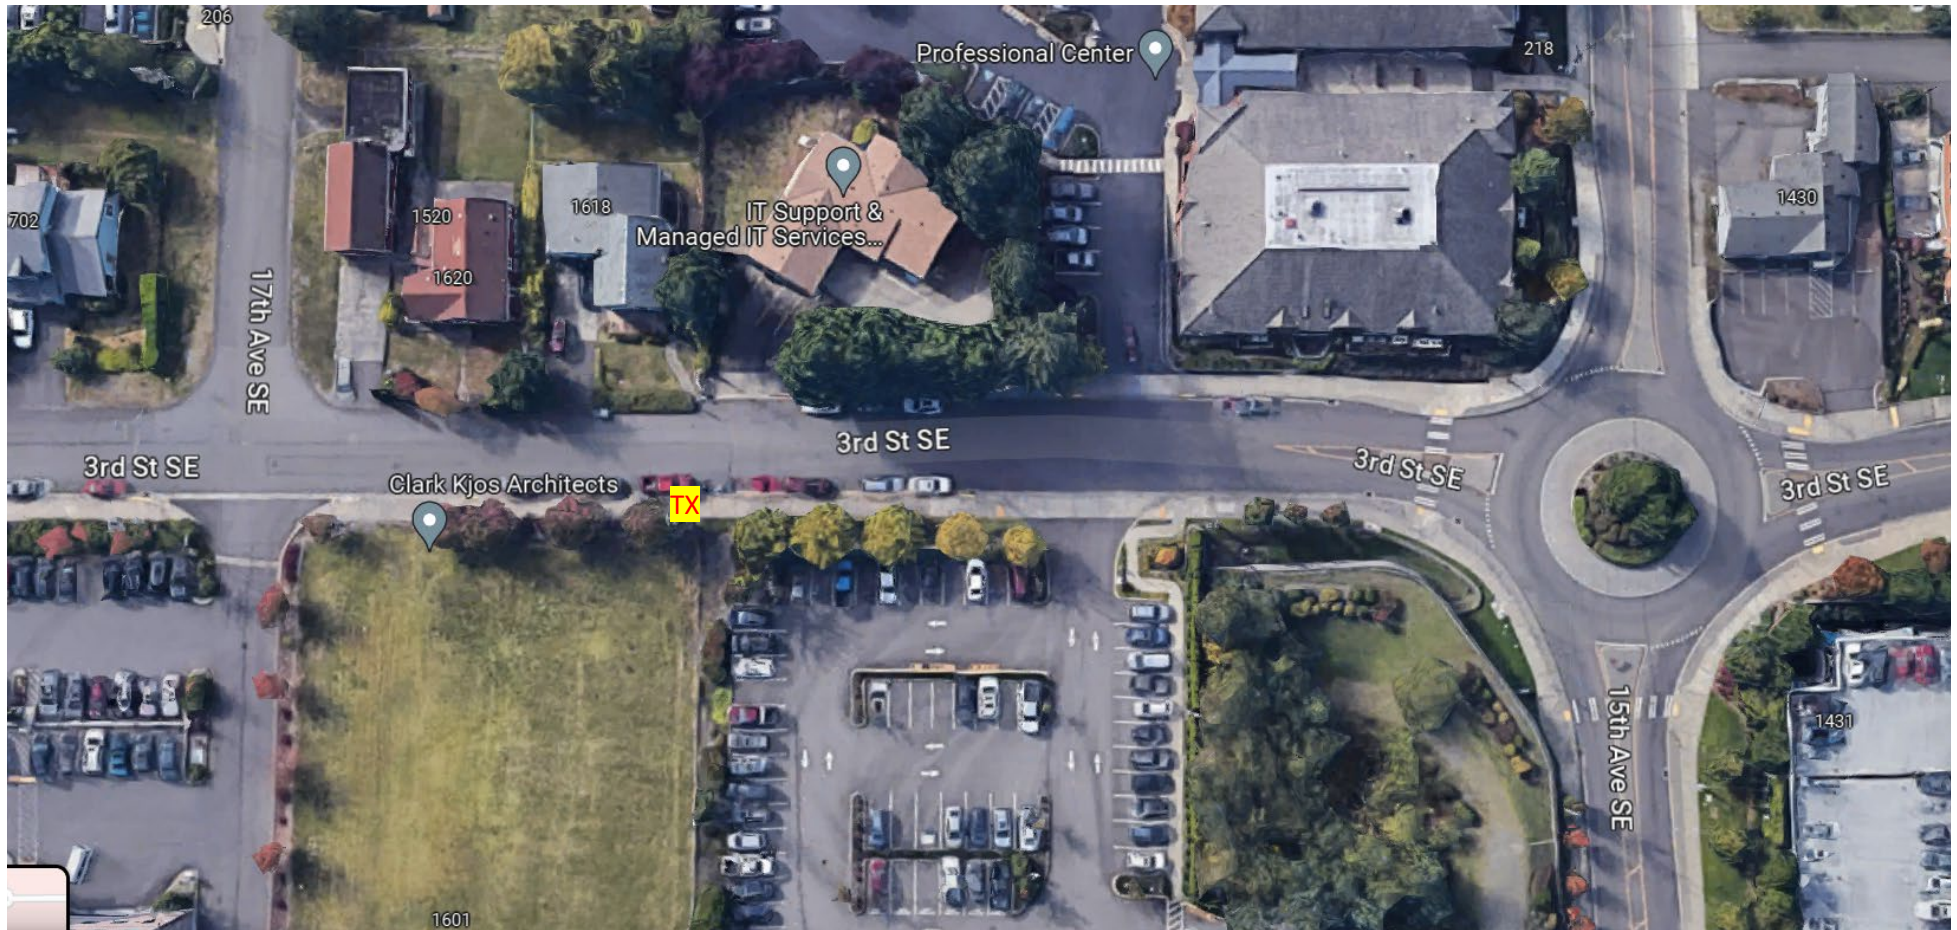

Transfer 3 cable attachments, 1 fiber cable attachment, 1 pole mount terminal, excavate existing facilities; Remove: 2 riser pipes, 7 aerial drops (425' each), 1 a crossarm; Install: 1 cable tag, 1 ground cable assembly, 1 fiber tag, 2 riser pipes (15' each), 7 aerial drops (500' each), a crossarm, copper cable placements in buried environment, splice copper connectors in buried environment.

Where a curb exists, the lateral offset of all vertical obstructions shall be a minimum of 1.5' from the face of the curb to the face of the vertical obstruction and a minimum of 3' at intersections. Where no curb exists, the lateral offset of all vertical obstructions shall be a minimum of 4' measured from the edge of pavement to the face of the obstruction.





